

***John F. Kennedy International Airport
Runway 13R-31L Reconstruction –
Project Update***

Committee on Construction


February 25, 2010



THE PORT AUTHORITY
OF NEW YORK & NEW JERSEY

Construction Schedule

Design Completion	February 2009
Contract Award:	June 2009
Site Preparation:	June 2009 to March 1, 2010
■ Full Runway Closure (10,700 ft):	March 1 to June 29, 2010
■ Runway intersection (500 ft):	September 16 to September 29, 2010
■ Portion of runway (3,300 ft):	July 1 to November 15, 2010
Taxiways & RSA	November 16, 2010 to November 15, 2011
Construction Completion	November 2011

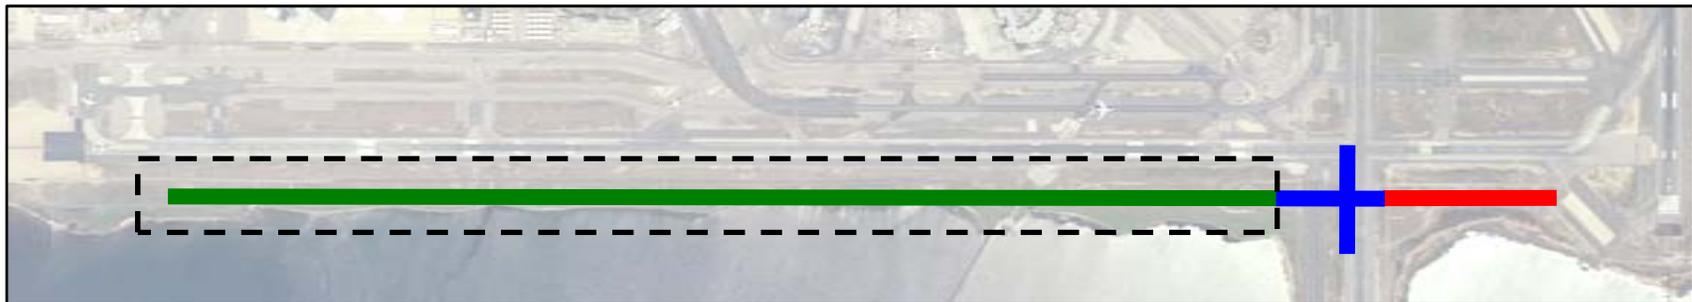

Planning and Site Preparation

- Ongoing communication with stakeholders
- Operating plan developed in coordination with airlines and FAA
- Contract incentives and penalties
- Mobilization of materials, equipment and labor




Test Section: Completion of Taxiway KC

- Demonstrated capability of the on-site concrete plant and slip-forming equipment
- Achieved level of production and quality of concrete for the project
- Demonstrated ability to minimize the impact of the construction activity on aeronautical operations




Scope of Work

- 263,000 yards of milling
- 151,000 cubic yards of concrete paving
- 220,000 tons of asphalt paving

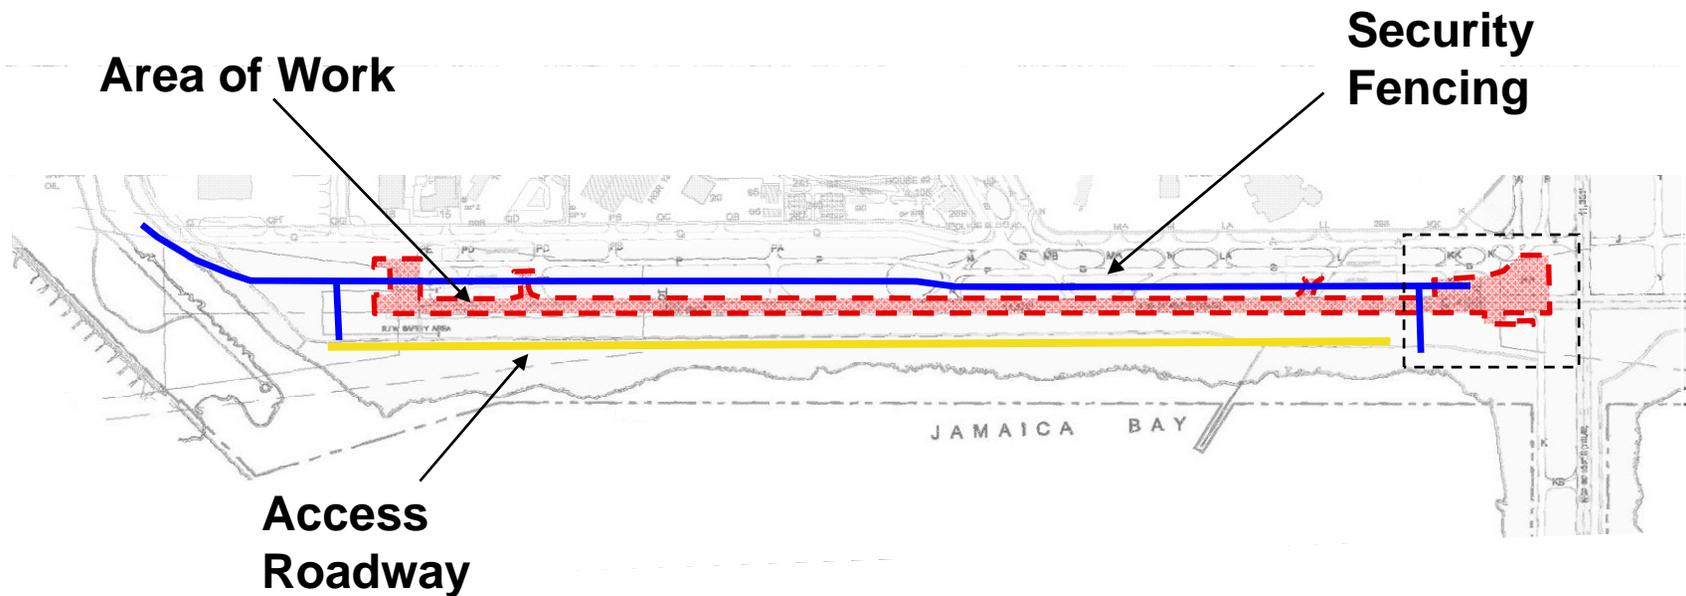


THE PORT AUTHORITY
OF NEW YORK & NEW JERSEY

Runway Cross Section

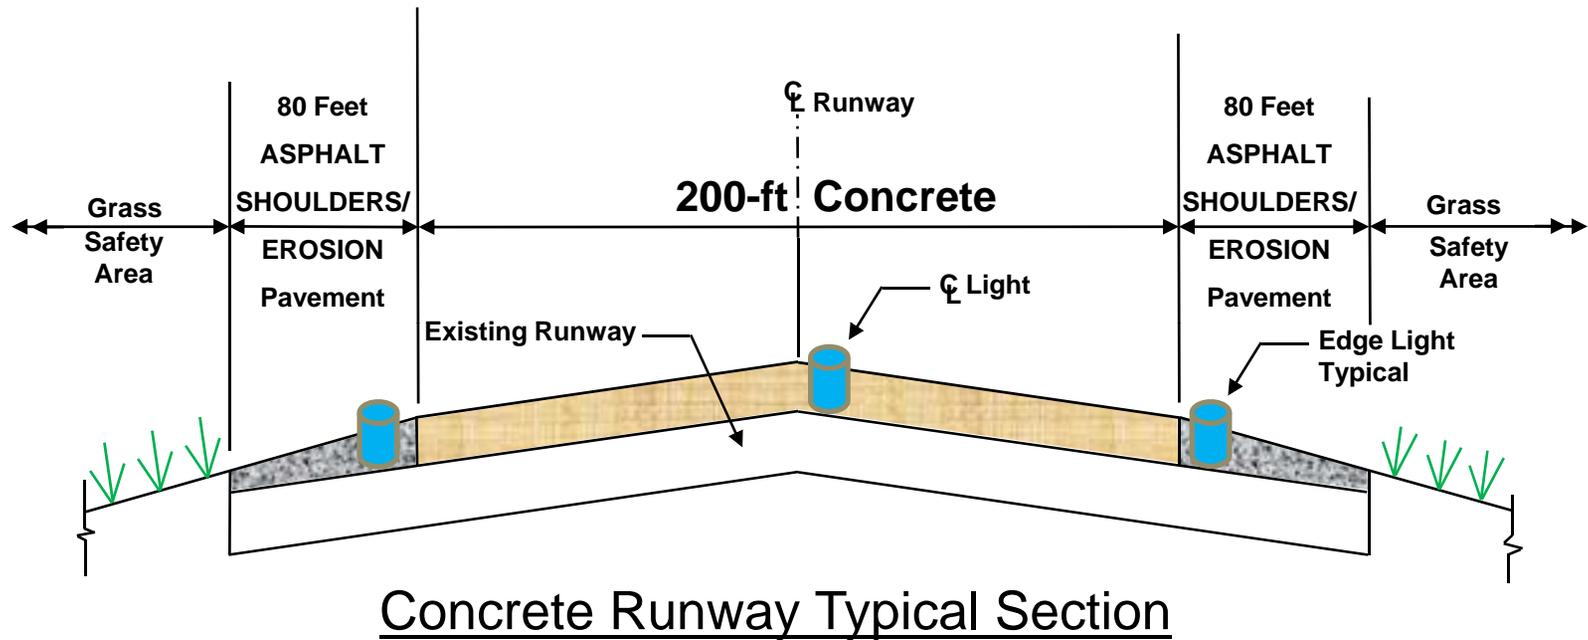

120 Day Closure: Construction Overview

- Paving sequencing plan
- Contingency days for weather and unforeseen conditions
- Careful monitoring of the schedule throughout the 120 day period

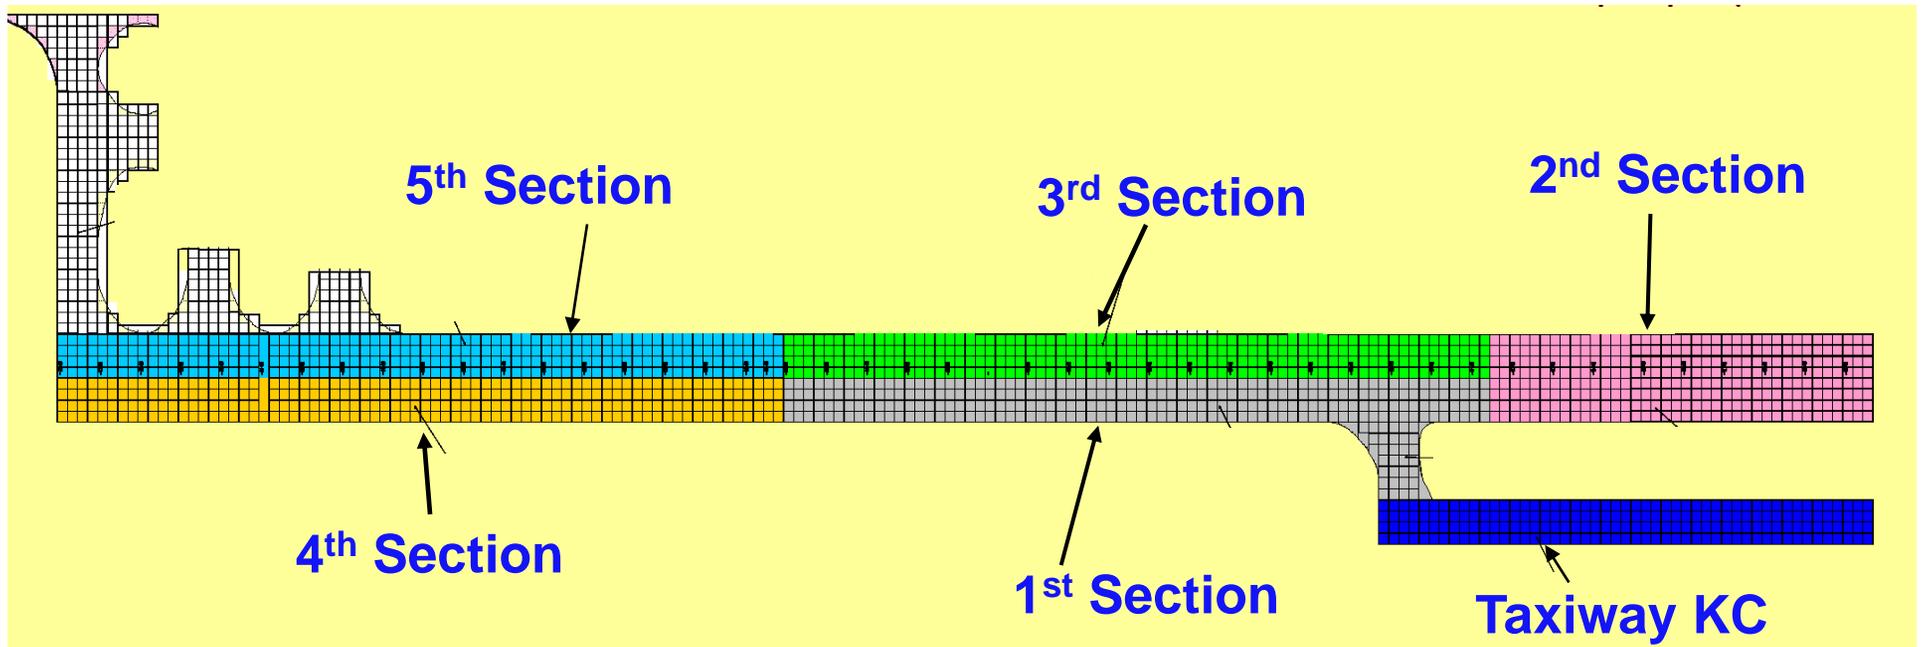

THE PORT AUTHORITY
OF NEW YORK & NEW JERSEY
