


Newark Liberty International Airport Terminal B Modernization Program Reauthorization

Committee on Construction

August 5, 2010

Terminal B Modernization Program Goals

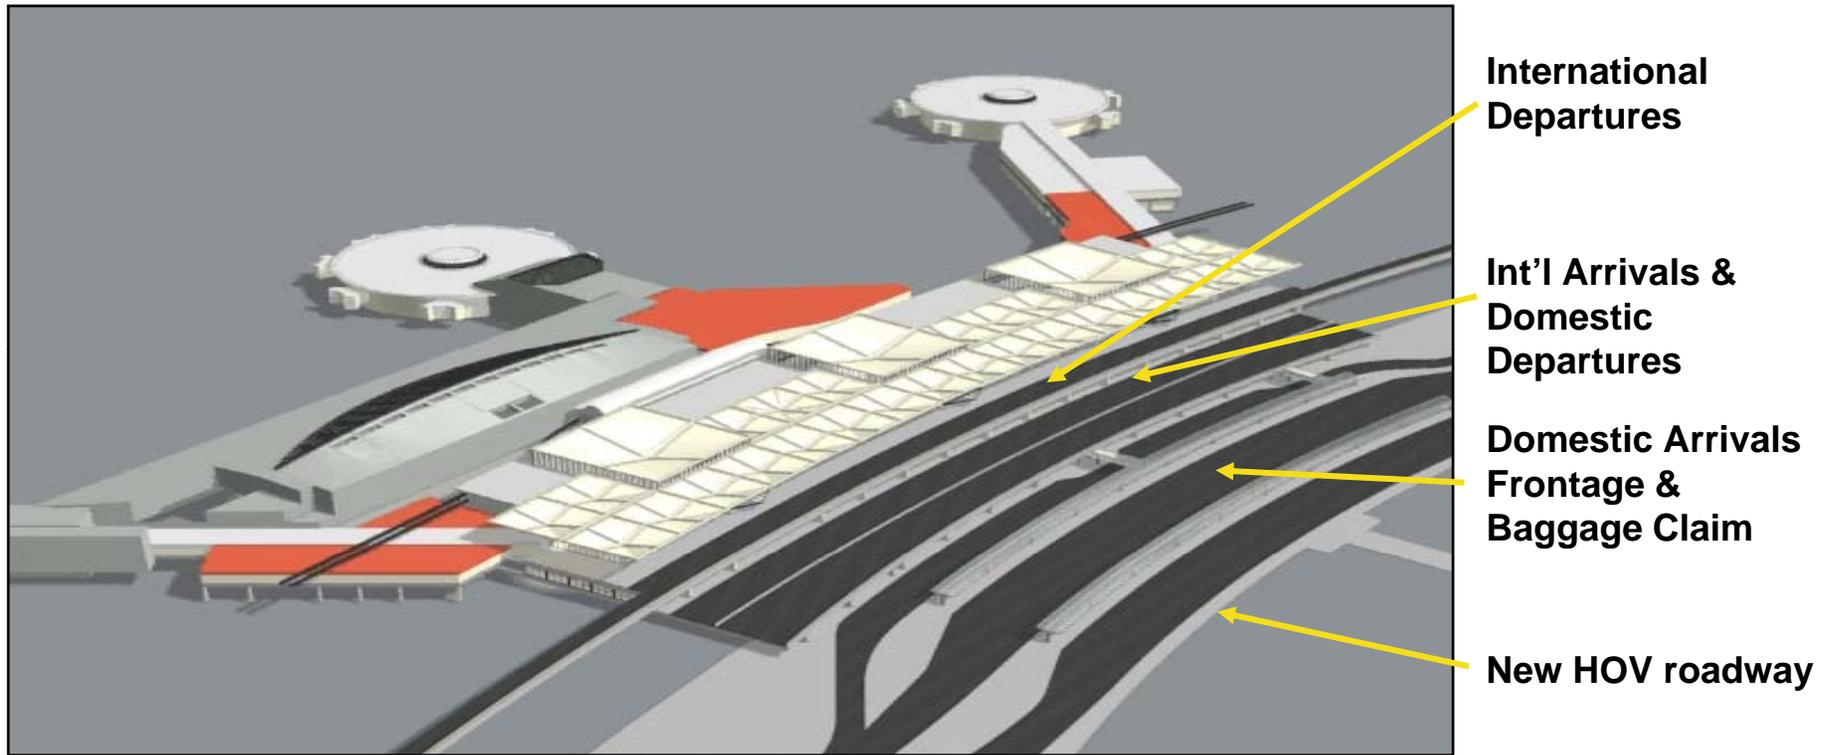

Program Goals:

- Reduce Congestion
- Relocate Domestic Baggage Claim
- Improve International Baggage Screening
- Expand Post-Security Concessions

Program Status



Lower Level Ticket Counter
- Completed Summer 2007

In-Line Baggage Screening
- Completed Summer 2009




Program Status - continued



Connectors Expansions –
Completed Spring 2010

Lower Level Expansion
- Fall 2010 Completion

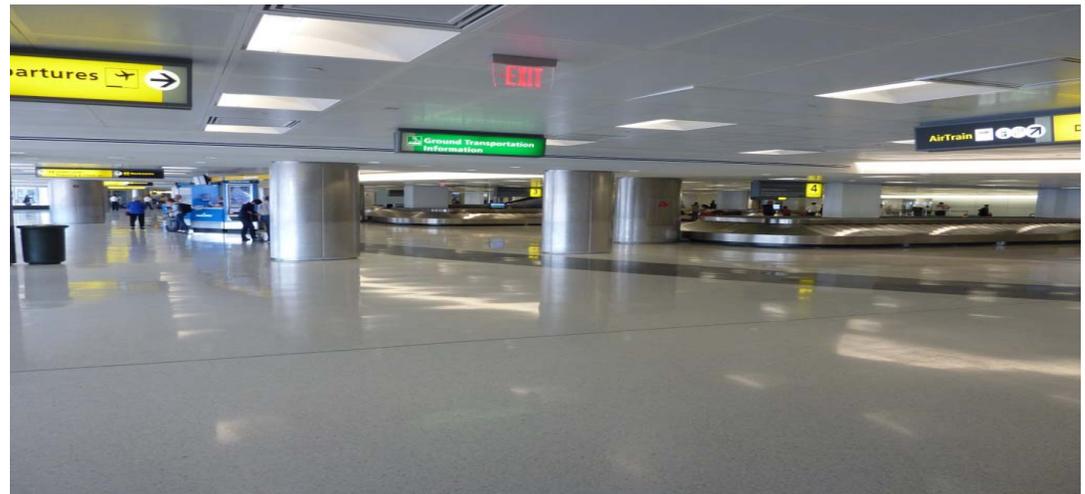

Program Status - continued



Mid & Upper Level -
Spring 2012 Completion

Meeter-Greeter - Design
Significantly Advanced



Program Challenges

In-Line Baggage & Security Changes	\$ 3.3 M
Power Distribution	\$ 7.8 M
Unforeseen Conditions (Utility relocations, AirTrain shutdowns)	\$ 7.3 M
<u>Increased Meeter-Greeter Capacity</u>	<u>\$ 4.1 M</u>
TOTAL	\$22.5 M

Program Cost Summary

Forecasted Completion Date	Summer 2013
Previously Authorized Amount	\$324.6 M
<u>Additional Funding Requested</u>	<u>\$ 22.5 M</u>
Total Project Reauthorization	\$347.1 M
